

Customer Portal — Outdoor Kitchens

Functional and visual specification of the customer-facing portal for outdoor-kitchen projects — the approved base design for all product types.

VERSION

1.1 · 17 August 2026

CLIENT

Tim & Bram · info@vanuitambacht.nl

ATTACHMENT

klantportaal-mockup.html (interactive mock-up)

RELATED

Quote-module brief v1.1 · bookkeeping brief

LANGUAGE NOTE — IMPORTANT

All customer-facing copy in the portal is Dutch and must be implemented literally as written in this brief. Dutch UI strings appear in quotation marks, with an English gloss in [brackets] for the developer's understanding only. The glosses must never appear in the product. There is no language switcher.

1 Purpose and principles

The customer portal is **not a mini-CRM for the customer**. It is the digital version of what Tim or Bram currently do over WhatsApp: show where the project stands, what is happening now, what is expected from the customer, and when delivery will take place. Guiding principle on every screen: **status** → **next step** → **action**. The attached interactive mock-up (`klantportaal-mockup.html`) is the approved design; this brief describes the behaviour behind it.

FIXED DECISIONS (BINDING FOR THE BUILD)

- **The portal only exists after the quote has been approved.** A portal account is by definition a project. Approval itself happens through the standalone quote link from the quote module (brief §7) — never inside the portal.
- **All product choices (including oil colour/finish) are made before approval** and are shown read-only in the portal.
- **The working drawing is view-only** — no approval flow — and the drawing card only renders when a drawing has actually been uploaded (no empty placeholder).
- **Delivery works proposal-first:** Vanuit Ambacht proposes one day + time slot; the customer approves it or requests a different day.

TWO HARD RULES

- **Every screen has exactly one primary action.** All other buttons are secondary (outline) or text links.
- **Never leak internal data:** no other projects, no subcontractor rates or margins, no internal notes, no file names or project codes on screen. The craftsman is never shown with contact details — all communication runs through Tim & Bram.

2 Access and phase transition

- **Trigger:** the moment a quote's status becomes **akkoord** [approved] in the dashboard, the system automatically creates portal access and sends a welcome message (e-mail + WhatsApp) containing a magic link.
- **Login:** magic link via e-mail/WhatsApp, no password. Token ≥ 128 bits of entropy, valid 90 days, reusable; same token logic as the quote-approval link.
- **Welcome copy (first login):** “Welkom Sander. Je opdracht staat — vanaf hier volg je alles: de bouw, de planning en de levering.” [Welcome Sander. Your order is confirmed — from here you follow everything: the build, the schedule and the delivery.]
- **One project per view.** If a customer has multiple projects, a simple project switcher appears in the header; data remains strictly separated per project (server-side filtering).

3 Navigation and status model

#	MENU ITEM (DUTCH, LITERAL)	ACTIVE	PURPOSE
1	Overzicht [Overview]	always	Status, next step, open actions
2	Mijn offerte [My quote]	always	Reference copy: review agreement, download PDF (read-only)
3	Ontwerp & opties [Design & options]	always	Review sizes, wood, options; view drawing (if uploaded)
4	Planning & levering [Schedule & delivery]	always	Timeline, approve delivery proposal, preparation
5	Foto's uit de werkplaats [Workshop photos]	always	Follow the build
6	Documenten [Documents]	always	Quote, drawing, terms, invoices, warranty
7	Betalingen [Payments]	always	Instalments, invoices, iDEAL
8	Berichten & contact [Messages & contact]	always	Thread + WhatsApp / call / e-mail
9	Oplevering & nazorg [Handover & aftercare]	after delivery	Handover check, warranty, maintenance, review

“Always” = from the first day the customer has access (i.e. after approval). Not-yet-active items remain visible but dimmed, with an explanatory line (“Beschikbaar zodra je keuken geleverd is” [Available once your kitchen is delivered]).

PROJECT PHASES (CUSTOMER VIEW)

Akkoord & ontwerp → In de werkplaats →
Klaar voor levering → Geleverd → Nazorg
[Approved & design → In the workshop → Ready for
delivery → Delivered → Aftercare]

The phase bar and timeline may show *Aanvraag* [Enquiry] and *Offerte* [Quote] as completed history. The quote has exactly one status inside the portal: “Akkoord gegeven op {date} om {time} door {name}”.

STATUS BADGES (IDENTICAL EVERYWHERE)

● Actie van jou — something is expected from the customer

✓ Afgerond / Betaald — done / paid (green)

Wij zijn aan zet — “our move”, stated explicitly

● Nieuw — new since last visit

4 Screen specifications

Per screen: content top-to-bottom, actions, statuses and data source. All dates written out in Dutch notation ("12 december 2026"); all amounts as € 1.960,00. Internal codes and file names never appear on screen.

4.1 Overzicht (home screen)

- **Greeting + project line:** "Hoi Sander" · product description · project number.
- **Status card (most important element):** horizontal phase bar, columns "Wat er nu gebeurt" [what's happening now] / "Wat er hierna komt" [what comes next], expected delivery week on the right.
- **Action block "Dit hebben we nog van je nodig"** [What we still need from you]: only when open actions exist; each action has a title, why, deadline, one button. With no actions: green rest card "Je hoeft nu niets te doen. Wij zijn aan zet — je hoort van ons zodra er nieuws is." Example actions: approve delivery proposal, pay 2nd instalment, confirm handover. Product choices never appear here (they were made before approval).
- **Latest workshop update** (photo + 1–2 lines) · **three tiles** (Delivery / Payment / Documents) · **compact timeline** · **contact block** Tim & Bram (WhatsApp primary; response promise "meestal binnen 2 uur, ook 's avonds" [usually within 2 hours, evenings included]).

Data source: project phase + delivery week (Projects/Planning), tasks of type *customer action*, latest photo, payment instalments, document counter.

4.2 Mijn offerte (reference copy, read-only)

- Quote card: number, date, badge ✓ Akkoord gegeven + "{date} om {time} door {name}" (from `akkoord.gegeven_op / akkoord.naam`).
- Line items with title + description + amount; `inbegrepen: true` → green label "Inbegrepen" [Included]. Totals card: subtotal excl. VAT / VAT 21% / total incl.
- Checklist "Inbegrepen bij jouw investering" · payment instalments with live payment status (50/50).
- Action bar: primary **"Volg je project"** [Follow your project]; secondary "Opdrachtbevestiging (pdf)", "Naar betalingen". Text line: "Deze offerte is vastgelegd. Wil je toch iets wijzigen? App ons — kleine wijzigingen kunnen vaak nog."
- Version history when multiple versions exist (older versions dimmed).

Data source: the quote JSON model 1-to-1 (read-only), including the approval block; payment status from the bookkeeping module. There is **no** approval flow inside the portal.

4.3 Ontwerp & opties (read-only)

- Large render/project photo, caption “Impressie op basis van jouw keuzes” [Impression based on your choices]. Four stat tiles (Size · Wood type · Cut-out · Lead time). Layout diagram with measurement line from `configuratie.diagram.segmenten`.
- “Jouw keuzes” [Your choices] grouped with check marks, including the pre-agreed oil colour. Options not chosen shown grey with text link “wil je de prijs weten?” [want to know the price?] — a gentle upsell, no prices shown.
- **Working drawing — view-only, conditional:** card with thumbnail, date, buttons “Tekening bekijken” / “Downloaden” / text link “Vraag over de tekening?”. **No approval button.** Hide the entire card while no drawing has been uploaded.
- Material info block (e.g. “Over Thermo Fraké”) from `configuratie.infobox`.

Data source: `configuratie` from the quote model + upload of type *drawing*. Status: only “Nieuw” on a fresh upload.

4.4 Planning & levering

- Expected delivery week, large + line “Wij doen een voorstel voor dag en tijdvak — goedkeuren kost je één klik.” [We propose a day and time slot — approving takes one click.] Badge “Op schema” [On schedule] / “Vertraagd” [Delayed].
- **Delivery proposal (core flow):** one concrete card with day + time slot. Primary “**Akkoord — plan deze dag in**” [Agreed — schedule this day]; below it a field “Past deze dag niet? Laat weten wanneer het wél uitkomt” + secondary “**Andere dag aanvragen**” [Request another day].
 - After approval: green confirmation “Afspraak vastgelegd: {day}, tussen {time}” + “Zet in mijn agenda” (.ics); the appointment is automatically fixed in the planning module.
 - After “Andere dag aanvragen”: status “Wacht op nieuw voorstel” [Awaiting new proposal]; the customer's wish becomes a dashboard task; a new proposal repeats the same flow.
- Vertical timeline (enquiry through aftercare; done/current/future, current step expanded with an explanation).
- “Zo verloopt de levering” [How delivery works] (4 points) + tickable checklist “Zo help je ons” [How you help us] (clearance ≥ 90 cm, level surface, someone home, parking) — ticks visible to Tim & Bram.
- **Delay:** always announced with reason and new expectation: “Het duurt iets langer dan gepland: {reden}. Nieuwe verwachting: {week}. Sorry — je hoort het meteen van ons.”

Data source: planning module (proposal dashboard → portal; approval/request portal → dashboard). Statuses: Op schema · Wacht op jouw akkoord (proposal) · Wacht op nieuw voorstel · Afspraak vastgelegd · Vertraagd.

4.5 Foto's uit de werkplaats

- Grid of **this project's photos only — filtered server-side on project id** (hard requirement; never client-side). Chronological, grouped per phase, “Nieuw” badge on unseen photos.
- Lightbox with previous/next (swipe on mobile), buttons “Downloaden” and “Delen” [Share].
- Block “Mag jouw keuken op onze Instagram?” [May your kitchen appear on our Instagram?] with customer photo upload (explicit consent).

Data source: Photos & media, filtered per project. Human titles; never internal photo numbers.

4.6 Documenten

- One list; per document: human title, category chip (Offerte / Contract / Tekening / Factuur / Voorwaarden / Handleiding / Garantie / Oplevering), full date, buttons Bekijken / Downloaden.
- Documents that do not exist yet are shown dimmed with an explanation (“Garantiebewijs — beschikbaar na levering”) — this makes the journey predictable.
- Display titles are always human; the technical file name may only exist in the download itself.

Data source: documents module + invoices from bookkeeping. Statuses: Nieuw · Nog niet beschikbaar.

4.7 Betalingen

- Summary: total · paid · outstanding + a simple progress bar.
- One card per instalment (from `investering.betaltermijnen`): percentage, moment, amount, status, date; button “Factuur bekijken”; when outstanding: **“Nu betalen (iDEAL)”**.
- Collapsible block for manual bank transfer (IBAN + reference = invoice number). Reassurance line: “Je betaalt nooit vooruit voor werk dat nog niet start.” [You never pay ahead for work that hasn't started.]
- Overdue variant stays friendly: “Deze staat nog open — vergeten kan gebeuren. Betaal in één klik.” Never red/threatening.

Data source: bookkeeping module (invoices, payment status, due date). Payment status can never be edited in the portal. Statuses: Betaald · Openstaand · Verwacht · Te laat.

4.8 Berichten & contact

- Message thread with Tim & Bram (sender, time, attachments/photos). **Every message triggers a WhatsApp/e-mail notification in both directions** — without notifications a portal thread is never read.
- Contact card: WhatsApp primary (deeplink `wa.me/31852129201` with prefilled message including the project number), call 06 82 00 80 25, e-mail `info@vanuitambacht.nl`.
- Block “Wij werken zonder showroom” [We deliberately have no showroom — keeps prices sharp] with button **“Stuur mij houtstalen”** [Send me wood samples].
- Block “Wie bouwt jouw keuken” [Who builds your kitchen]: the craftsman without contact details; “Alles regel je via ons.” [You arrange everything through us.]
- 4–6 FAQs, collapsible.

Data source: per-project message log (both directions). Statuses: Nieuw antwoord · Gelezen · Verzonden.

4.9 Oplevering & nazorg (active after delivery)

- Heading “Geleverd op {date}. Veel kookplezier.” [Delivered on {date}. Happy cooking.] + final photo.
- **Handover confirmation:** checklist (complete, no damage, everything works, instructions received) + primary “Alles klopt — bevestigen” [All good — confirm]. Alternative “Er is iets niet goed” → field + photo upload → automatically a dashboard task.
- Warranty & aftercare: warranty certificate download, button “Nazorg aanvragen” [Request aftercare]. Maintenance tips + guide + opt-in spring reminder.
- Review block (Google / Instagram) and one calm cross-sell card (canopy / garden room / poolhouse).

Data source: handover record, warranty data; an aftercare report becomes a task. Statuses: Wacht op jouw bevestiging · Opgeleverd & bevestigd · Nazorg in behandeling.

5 Component library

COMPONENT	USE	VARIANTS
StatusBadge	phase and action statuses	action (bronze) · done (green) · waiting (sand) · new (blue)
PhaseTracker	horizontal phase bar	full on desktop; “step 4 of 6” + bar on mobile
ActionCard	open customer action	with/without deadline; always exactly one button
RestCard	“nothing to do right now”	green, with explanatory line
SummaryTile	small card label + value + sub-status	delivery / payment / documents
TimelineItem	timeline step	done · current (expanded) · future (dimmed)
SpecTile	configuration stat tile	4 per row desktop, 2 per row mobile
LayoutDiagram	layout diagram + measurement line	cabinet / cut-out; widths proportional
ChoiceRow	chosen / not-chosen option	green check · grey + price-on-request link
DrawingCard	working drawing, view-only	render only when an upload exists; new-badge
ProposalCard	delivery proposal	awaiting approval · fixed (green + .ics) · awaiting new proposal
DocumentRow	document in list	available · not yet available (dimmed)
PaymentTerm	payment instalment	paid · outstanding · expected · overdue
PhotoCard + Lightbox	workshop photos	new-badge; swipe on mobile
MessageBubble	message in thread	from us / from customer; with attachment
ContactBlock	Tim & Bram	WhatsApp primary · call · e-mail

Interactions: visible hover/focus states (keyboard accessible), success actions with a short inline confirmation (no browser alerts), confirming actions (handover, delivery proposal) always behind a confirmation step.

6 Copy (implement literally, in Dutch)

The portal is 100% Dutch, informal je/jij form, written the way Tim & Bram text: short, warm, direct. No search bar, no language switcher, no English breadcrumbs. English in [brackets] below = gloss only, never shipped.

Screen titles: Overzicht · Mijn offerte · Ontwerp & opties · Planning & levering · Foto's uit de werkplaats · Documenten · Betalingen · Berichten & contact · Oplevering & nazorg

Status labels: “Actie van jou” [action for you] · “Wij zijn aan zet” [our move] · “Op schema” [on schedule] · “Akkoord gegeven” [approval given] · “Wacht op jouw akkoord” (delivery proposal only) · “Wacht op nieuw voorstel” · “Afspraak vastgelegd” · “Betaald” · “Openstaand” · “Nieuw” · “Beschikbaar na levering”

Buttons: “Volg je project” · “Opdrachtbevestiging (pdf)” · “Downloaden” · “Tekening bekijken” · “Ik heb nog een vraag” · “Akkoord — plan deze dag in” · “Andere dag aanvragen” · “Zet in mijn agenda” · “Nu betalen (iDEAL)” · “Factuur bekijken” · “WhatsApp ons” · “Stuur mij houtstalen” · “Alles klopt — bevestigen” · “Nazorg aanvragen” · “Review achterlaten”

System messages:

- Rest: “Je hoeft nu niets te doen. Wij zijn aan zet — je hoort van ons zodra er nieuws is.”
- Action: “Er wacht 1 ding op jou. Dat kost je één minuut.”
- Welcome: “Welkom {first name}. Je opdracht staat — vanaf hier volg je alles: de bouw, de planning en de levering.”
- Delay: “Het duurt iets langer dan gepland: {reason}. Nieuwe verwachting: {week}. Sorry — je hoort het meteen van ons.”
- No showroom: “We hebben geen showroom. Dat houdt onze prijzen scherp en jouw keuken beter. Wil je hout in het echt zien? We sturen gratis stalen op.”

7 Desktop and mobile

MUST BE FLAWLESS ON MOBILE

- Overview: status card + action block (actions on top)
- Reviewing the quote + PDF download
- Approving the delivery proposal
- Photos with swipe lightbox
- Messages + WhatsApp button (always in the bottom bar)
- Paying with iDEAL

TECHNICAL REQUIREMENTS

- Breakpoints 1200 / 900 / 600 px
- Sidebar → fixed bottom bar with 5 icons below 900 px (Overzicht · Offerte · Planning · Foto's · Contact; rest behind “Meer”)
- Tables become cards below 600 px
- Touch targets minimum 44 × 44 px; one-handed use
- Sticky bottom action bar on screens with a primary action

8 Data coupling dashboard ↔ portal

CUSTOMER PORTAL	SOURCE IN THE DASHBOARD	DIRECTION
Create portal access	trigger: quote status → akkoord ⇒ send magic link	dashboard → portal
Phase & progress	Projects → status/phase	dashboard → portal
Expected delivery week	Planning → delivery date	dashboard → portal
Quote, lines, totals, instalments	Quote module (JSON model, read-only)	dashboard → portal
Approval data (name, time, IP, version)	Quote module akkoord — filled via the quote link	dashboard → portal
Open customer actions	Tasks of type <i>customer action</i>	dashboard → portal
Delivery proposal (day + slot)	Planning module → proposal per project	dashboard → portal
Proposal approval / other-day request / handover check	task ticked + log line on the project	portal → dashboard
Working drawing	Documents → upload of type <i>drawing</i> ; card only when an upload exists	dashboard → portal
Photos	Photos & media, server-side filtered per project	dashboard → portal
Documents & invoices	Documents + bookkeeping	dashboard → portal
Payment status	Bookkeeping (invoices)	dashboard → portal
Messages	Communication log per project	both directions
Aftercare report	automatically becomes a task	portal → dashboard

NOTIFICATIONS (ESSENTIAL)

Every new customer action, new photos, new document and new message sends one short WhatsApp or e-mail notification with **a single deep link to the right screen**. Tone: short and personal, as if Tim or Bram typed it. Without these notifications the portal will not be visited and the concept fails.

9 Build order (recommendation)

- **Phase 1 — biggest impact, smallest build:** automatic portal access on approval · Overview (status + actions) · Messages & contact · notifications. This immediately replaces the “how is it going?” WhatsApp messages.
- **Phase 2:** Schedule & delivery (proposal approval) · Photos · Documents · Payments (iDEAL).
- **Phase 3:** Design & options (reference + drawing view) · Handover & aftercare · review flow.
- **Later:** AI renders instead of SketchUp drawings — only the image on screen 4.3 changes, not the structure.

10 Acceptance criteria


- 1. Portal access is created exclusively and automatically when a quote reaches status **akkoord**; the customer receives the magic link within 1 minute.
- 2. A customer can never see data from another project or customer — photo filtering demonstrably server-side (test with two projects).
- 3. The portal contains no editable product choice and no approval button for the quote or the drawing.

- 4. The drawing card is invisible while no drawing is uploaded, and appears (with “Nieuw” badge + notification) after upload.
- 5. The proposal flow works end-to-end: proposal set in the dashboard → customer approves → appointment fixed in the planning module → .ics correct; the other-day route automatically creates a task.
- 6. All amounts and dates in Dutch notation; all copy from chapter 6 implemented literally; no internal codes or file names anywhere on screen.
- 7. Every event from chapter 8 sends exactly one notification with a deep link to the right screen.
- 8. Payment status comes live from the bookkeeping module; an iDEAL payment shows as “Betaald” within 1 minute.
- 9. The five mobile core flows (ch. 7) work on a 375 px wide device, with sticky action bar and bottom-bar navigation.
- 10. Handover confirmation and aftercare reports automatically create a task/log line in the dashboard.

Vanuit Ambacht · vanuitambacht.nl · info@vanuitambacht.nl · +31 85 212 9201 — Questions about this brief? Message or e-mail Tim & Bram.
Attachment: [klantportaal-mockup.html](#) (the approved visual design; when in doubt the mock-up leads for visuals and this brief leads for behaviour).

Annex — Visual design (screenshots from the approved mock-up)

The screens below come 1-to-1 from the attached interactive mock-up and show what the portal must look like. The mock-up leads for colours, typography (Playfair Display + Montserrat), spacing and components; this brief leads for behaviour. Photo areas are placeholders. All UI copy is Dutch by design.

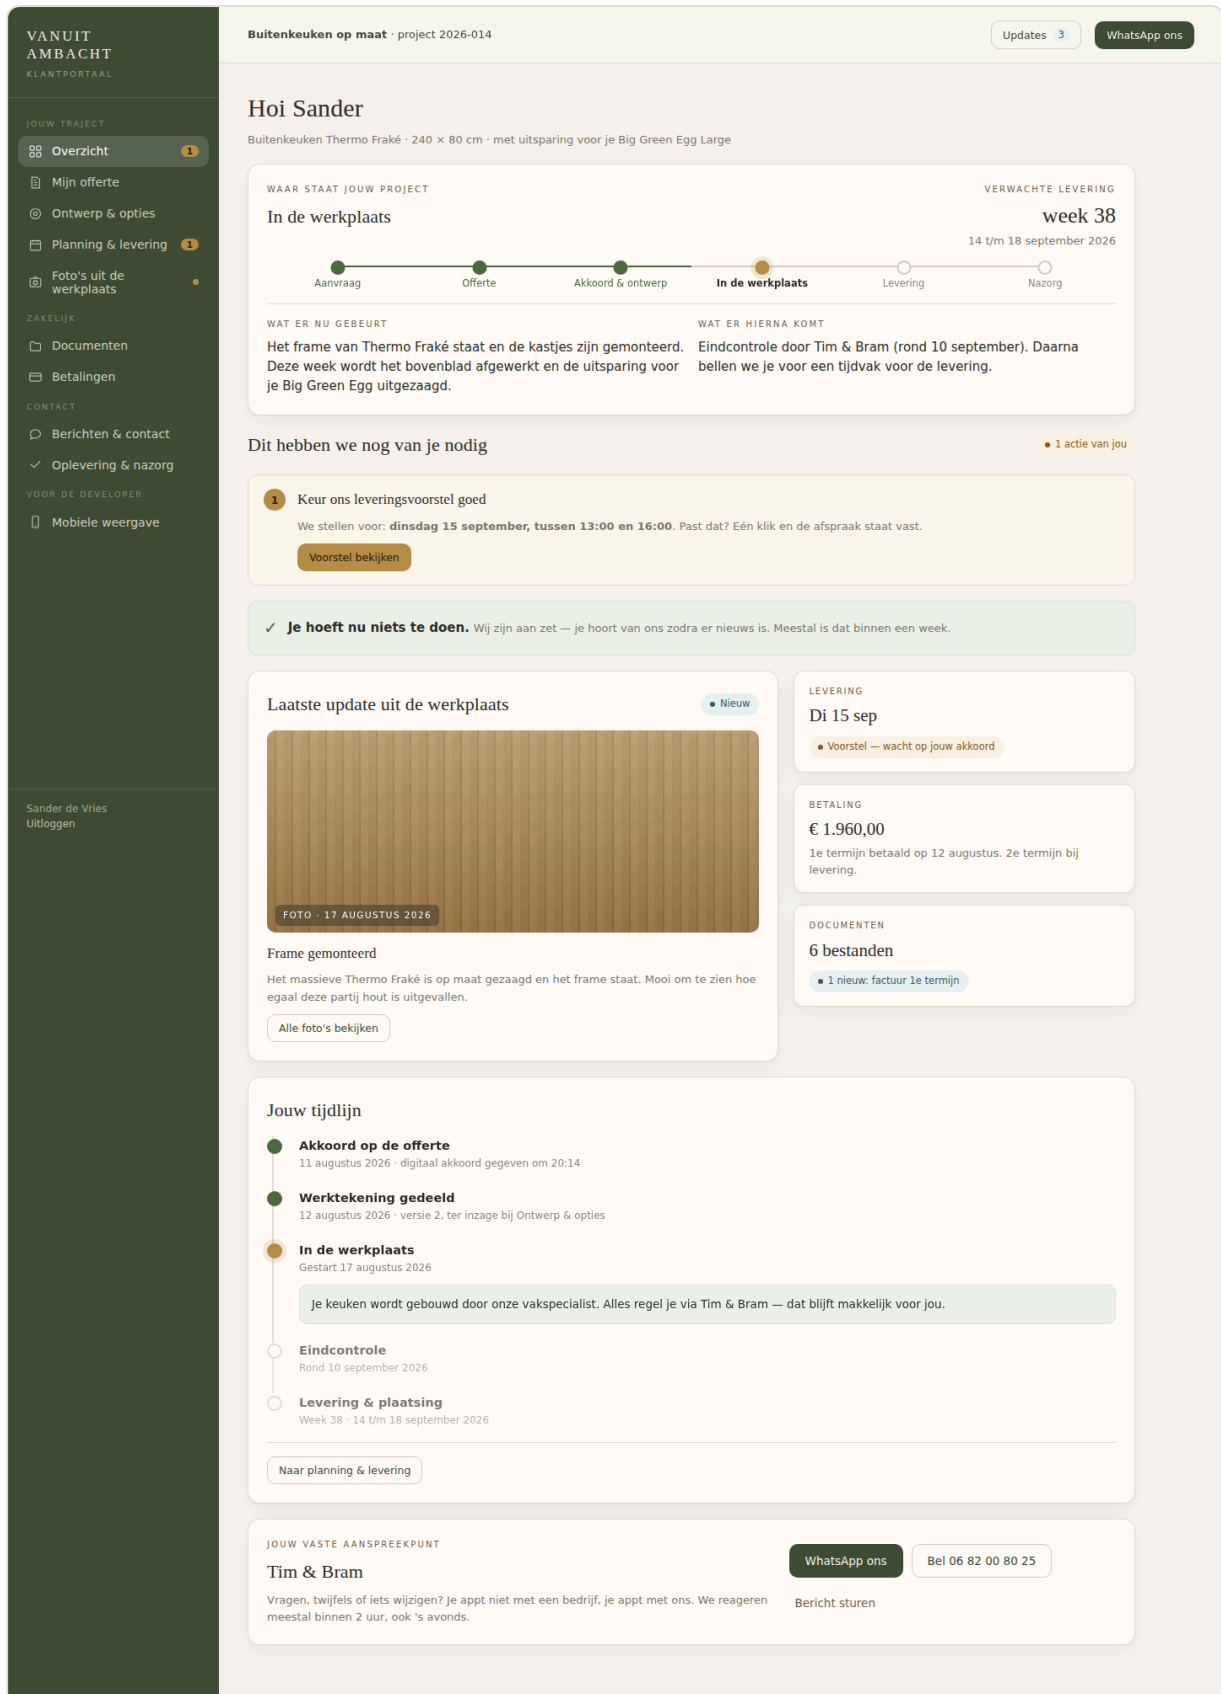

Screen 1 — Overview. Note: the action block and the green rest card are both pictured here; in the real portal exactly one of the two is visible at any time.

VANUIT
AMBACHT

KLANTPORTAAL

JOUW TRAJECT

Overzicht

Mijn offerte

Ontwerp & opties

Planning & levering

Foto's uit de werkplaats

ZAKELIJK

Documenten

Betalingen

CONTACT

Berichten & contact

Oplevering & nazorg

VOOR DE DEVELOPER

Mobiele weergave

Sander de Vries

Uitloggen

Buitenkeuken op maat · project 2026-014

Updates 3

WhatsApp ons

Mijn offerte

Dit is wat we hebben afgesproken. Alles nog eens rustig nalezen? De pdf staat ook bij je documenten.

OF-2026325

Akkoord gegeven

11 augustus 2026 om 20:14 door Sander de Vries

Buitenkeuken Thermo Fraké · 240 × 80 cm

Opgemaakt op 21 juli 2026 voor Sander de Vries, Oisterwijk

WAT JE KRIJGT

Buitenkeuken Thermo Fraké · 240 × 80 cm

€ 3.495,00

Houten bovenblad met keramische stenen, uitsparing voor Big Green Egg Large, twee kastjes met lades, afgewerkt met twee lagen olie.

Kraan & wasbak

€ 425,00

Inbouwkraan met spoelbak, aansluiting op je buitenkraan.

Bezorging Oisterwijk

Inbegrepen

Levering en plaatsing op een moment dat jou uitkomt, door twee man.

INBEGREPEN BIJ JOUW INVESTERING

✓ Werktekening van jouw keuken, in te zien in dit portaal

✓ Bouw door een gecertificeerde vakspecialist uit ons netwerk

✓ Gratis bezorging en plaatsing in Oisterwijk

✓ Uitleg en eerste onderhoud bij levering

✓ Garantie op het product én nazorg na levering

Subtotaal excl. btw

€ 3.239,67

Btw 21%

€ 680,33

Totaal

€ 3.920,00

BETALEN IN TWEE STAPPEN

50% bij akkoord

€ 1.960,00

Betaald op 12 augustus. Hiermee is de order uitgezet bij de vakspecialist.

50% bij levering

€ 1.960,00

Je betaalt nooit vooruit voor werk dat nog niet start.

Volg je project

Opdrachtbevestiging (pdf)

Naar betalingen

Deze offerte is vastgelegd. Wil je toch iets wijzigen? App ons — kleine wijzigingen kunnen vaak nog.

EERDERE VERSIES

Offerte OF-2026311 · versie 1

14 juli 2026 · vervangen door versie 2 (maat aangepast naar 240 cm)

Bekijken

Screen 2 — My quote (reference copy, read-only, status “Akkoord gegeven”).

VANUIT
AMBACHT

KLANTPORTAAL

JOUW TRAJECT

Overzicht

Mijn offerte

Ontwerp & opties

Planning & levering

Foto's uit de werkplaats

ZAKELIJK

Documenten

Betalingen

CONTACT

Berichten & contact

Oplevering & nazorg

VOOR DE DEVELOPER

Mobiele weergave

Sander de Vries
Uitloggen

Buitenkeuken op maat · project 2026-014

Updates 3

WhatsApp ons

Ontwerp & opties

Dit is wat we voor je bouwen, precies zoals afgesproken in de offerte. Zie je toch iets gekst? App ons even.

RENDER · JOUW ONTWERP

Impressie op basis van jouw keuzes. Kleur en houttekening kunnen in het echt licht afwijken — hout is natuurlijk materiaal.

INDELING · VAN LINKS NAAR RECHTS

kastje met lades

kastje met lades

uitsparing Big Green Egg

kastje open vak

0 cm240 cm

Jouw keuzes

BOVENBLAD

- ✓ Houten bovenblad met keramische stenen inleg
- ✓ Uitsparing Big Green Egg Large, rechts van het midden

INDELING & OPBERGRUIMTE

✓ Twee kastjes met lades op softclose

✓ Eén open vak voor hout of accessoires

WATER & KOELING

✓ Kraan & wasbak met aansluiting op de buitenkraan

Koelkast

niet gekozen

wil je de prijs weten?

AFWERKING & BEZORGING

✓ Twee lagen olie, kleur naturel

✓ Zwenkwielen met rem, zodat je hem kunt verplaatsen

✓ Gratis bezorgd en geplaatst in Oisterwijk

AFMETING

240 × 80

centimeter

HOUTSOORT

Thermo Fraké

levensduur 20 tot 25 jaar

UITSPARING

Big Green Egg

Large, rechts van het midden

LEVERTIJD

3 tot 5 weken

na jouw akkoord

OVER THERMO FRAKÉ

Thermisch gemodificeerd hout: door verhitting krimpt en werkt het nauwelijks, zonder chemie. Vergrijst mooi egaal en gaat 20 tot 25 jaar mee.

WERKTEKENING

Nieuw

TEKENING · VERSIE 2


Gedeeld op 12 augustus 2026. Hierop staan de maten, de indeling en de plek van de uitsparing — ter inzage, zodat je precies weet wat er gebouwd wordt.

Tekening bekijken

Downloaden

Vraag over de tekening?

Screen 3 — Design & options (read-only; working drawing view-only, card only rendered when uploaded).

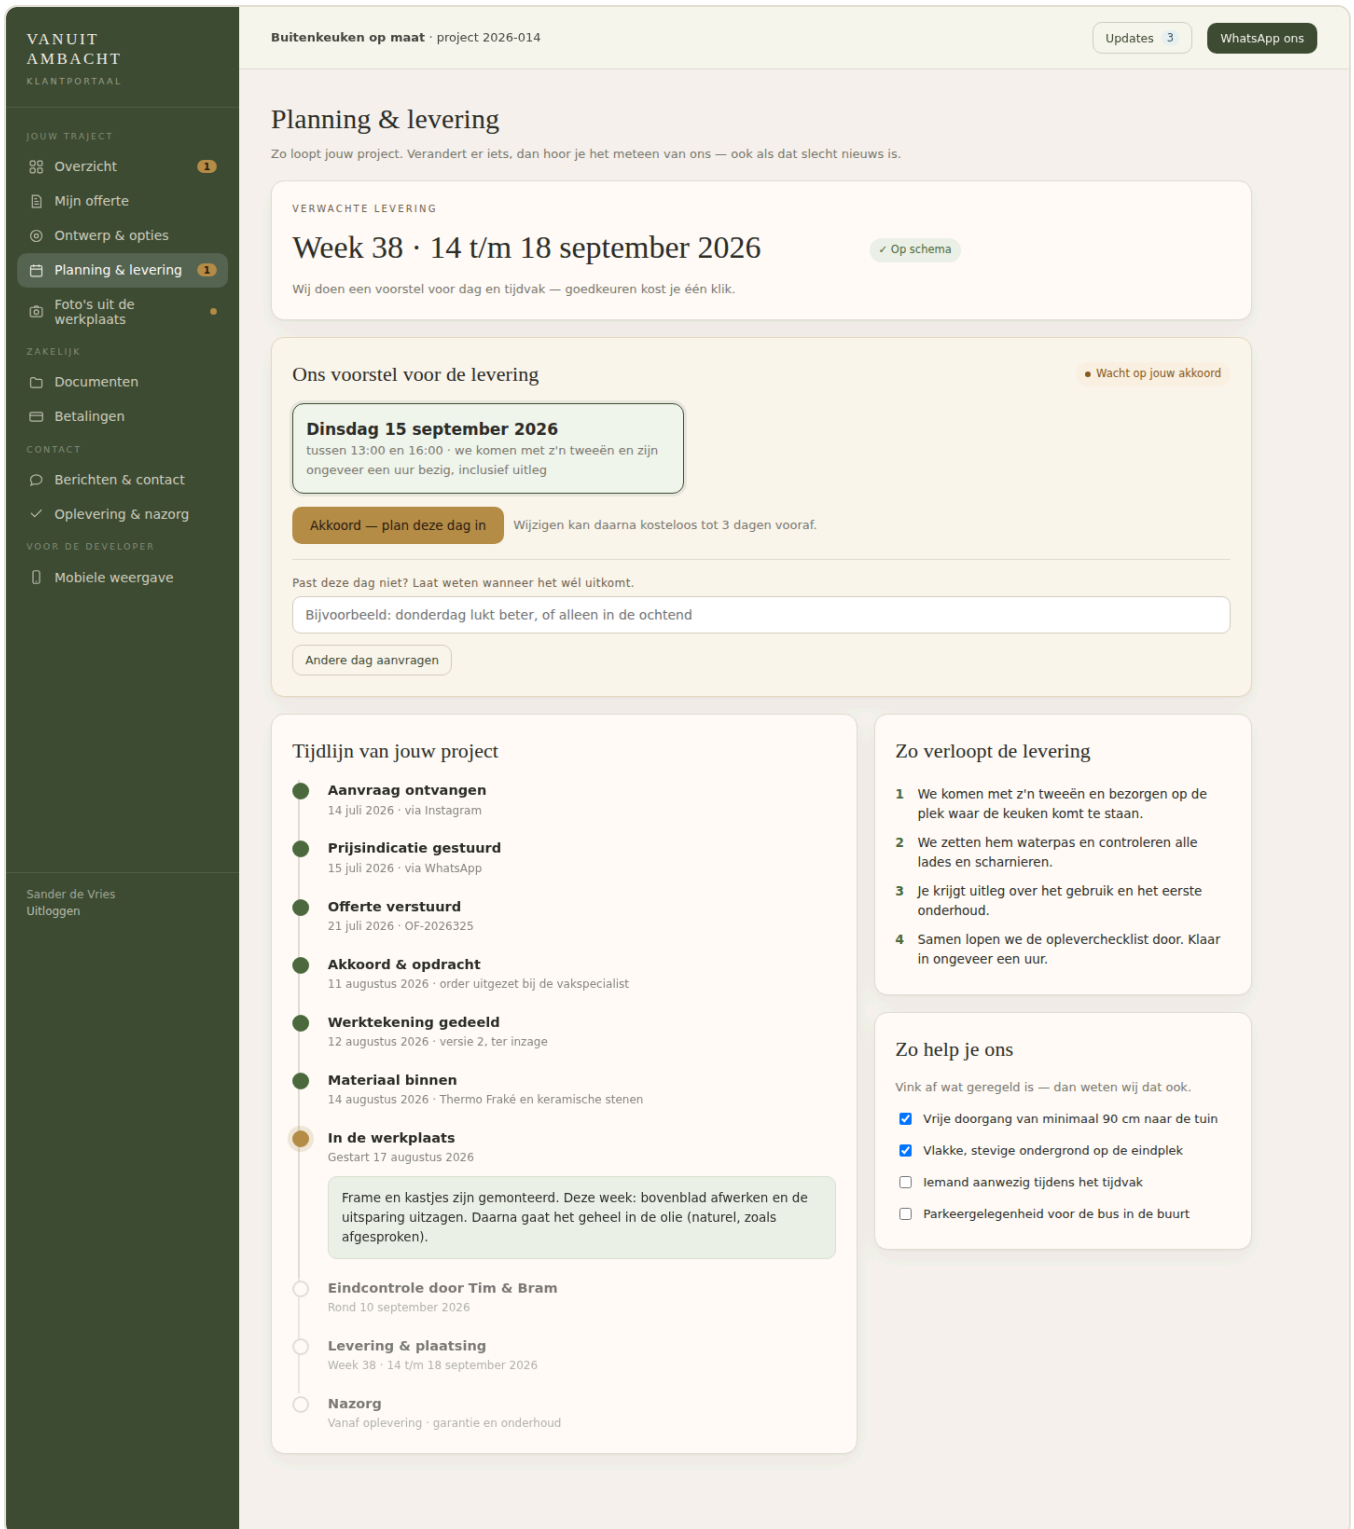

Screen 4 — Schedule & delivery, with the delivery proposal (proposal-approval flow).

VANUIT
AMBACHT
KLANTPORTAAL

JOUW TRAJECT

Overzicht1

Mijn offerte

Ontwerp & opties

Planning & levering1

Foto's uit de werkplaats•

ZAKELIJK

Documenten

Betalingen

CONTACT

Berichten & contact

Oplevering & nazorg

VOOR DE DEVELOPER

Mobiele weergave

Sander de Vries
Uitloggen

Buitenkeuken op maat · project 2026-014

Updates3WhatsApp ons

Foto's uit de werkplaats

Zo ontstaat jouw keuken. We sturen een berichtje zodra er nieuwe foto's zijn.

IN DE WERKPLAATS · AUGUSTUS 2026

17 AUGUSTUS

Frame gemonteerd

Nieuw

Het frame staat en de kastjes zijn ingehangen. Volgende stap: het bovenblad.

15 AUGUSTUS

Op maat gezaagd

Nieuw

Alle delen zijn op maat gezaagd. 240 cm, precies zoals op de tekening.

14 AUGUSTUS

Materiaal binnen

De partij Thermo Fraké is binnen en gecontroleerd op kleur en kwaliteit.

NOG TE KOMEN

VERWACHT BEGIN SEPTEMBER

Bovenblad & uitsparing

VERWACHT 10 SEPTEMBER

In de olie & eindcontrole

VERWACHT WEEK 38

Bij jou in de tuin


Mag jouw keuken op onze Instagram?

Heb je zelf een mooie foto gemaakt? Stuur hem op. We plaatsen nooit iets zonder jouw toestemming, en je adres of naam komt er niet bij te staan.

ja, hier is een foto

Liever niet

Screen 5 — Workshop photos (own project only).

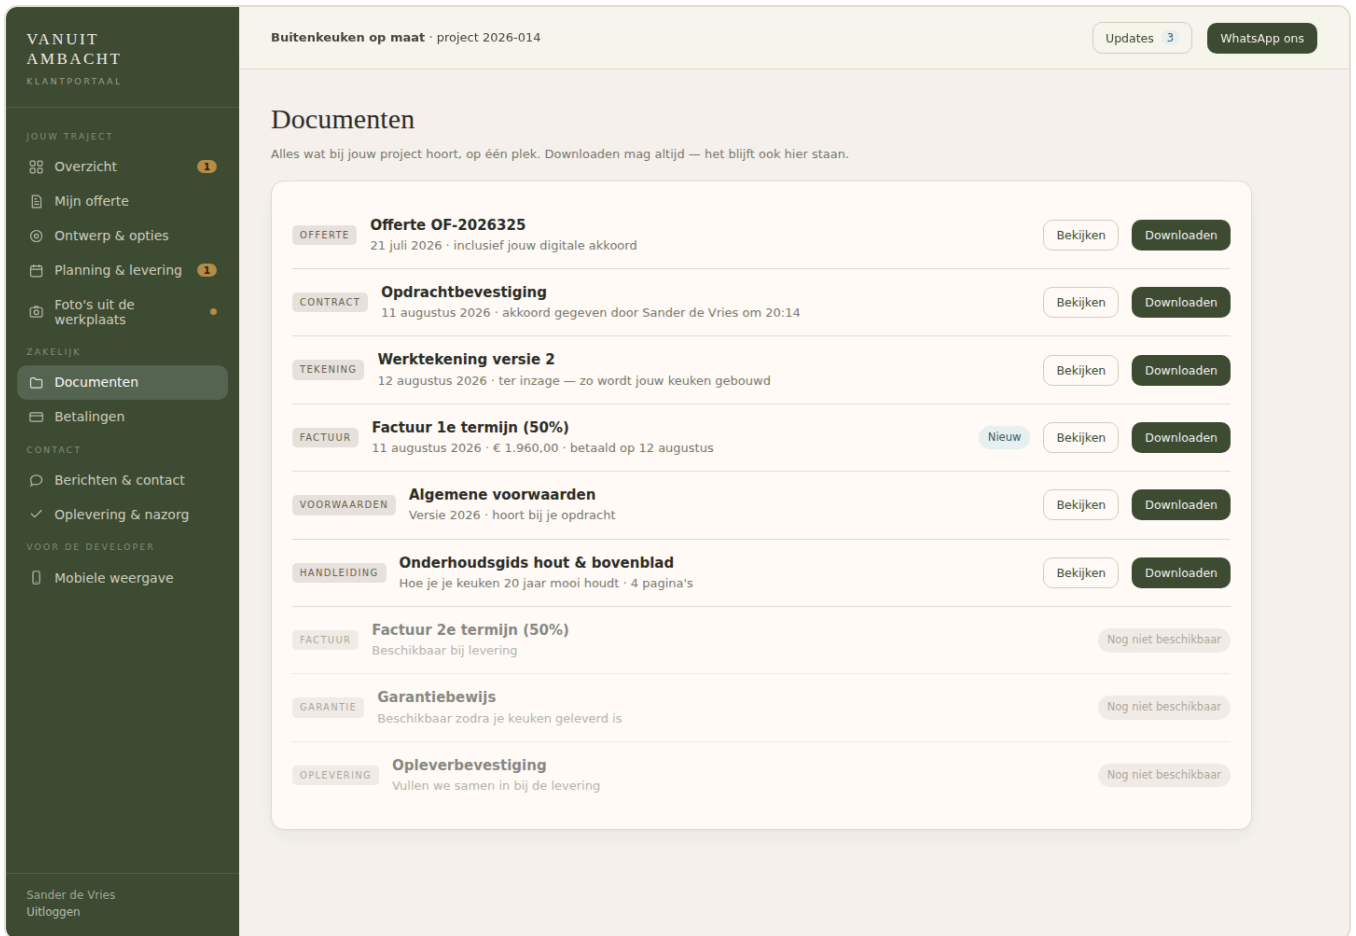

Screen 6 — Documents (human titles; future documents dimmed).

VANUIT
AMBACHT

KLANTPORTAAL

JOUW TRAJECT

Overzicht

Mijn offerte

Ontwerp & opties

Planning & levering

Foto's uit de werkplaats

ZAKELIJK

Documenten

Betalingen

CONTACT

Berichten & contact

Oplevering & nazorg

VOOR DE DEVELOPER

Mobiele weergave

Sander de Vries

Uitloggen

Buitenkeuken op maat · project 2026-014

Updates 3

WhatsApp ons

Betalingen

Twee termijnen, geen verrassingen. Je betaalt nooit vooruit voor werk dat nog niet start.

TOTAAL

€ 3.920,00

incl. btw

BETAALD

€ 1.960,00

op 12 augustus 2026

NOG TE BETALEN

€ 1.960,00

bij levering

1e termijn · 50% bij akkoord

Betaald

€ 1.960,00

Ontvangen op 12 augustus 2026. Hiermee is de order uitgezet bij de vakspecialist.

Factuur bekijken

2e termijn · 50% bij levering

Volgt bij levering

€ 1.960,00

Je ontvangt de factuur op de dag van levering. Betalen kan met iDEAL of overboeking, binnen 14 dagen.

Nu betalen (iDEAL)

Liever zelf overmaken?

Dat kan. Gebruik het factuurnummer als kenmerk, dan kunnen wij het goed verwerken.


IBAN NL27 ABNA 0132 2698 56
t.n.v. Vanuit Ambacht · Vleuten

Vraag over een factuur?


App of bel ons — we zoeken het meteen op. Je hoeft geen formulier in te vullen.

WhatsApp ons


Screen 7 — Payments (50/50 instalments, iDEAL).



Screen 8 — Messages & contact (thread, no-showroom block, wood samples).

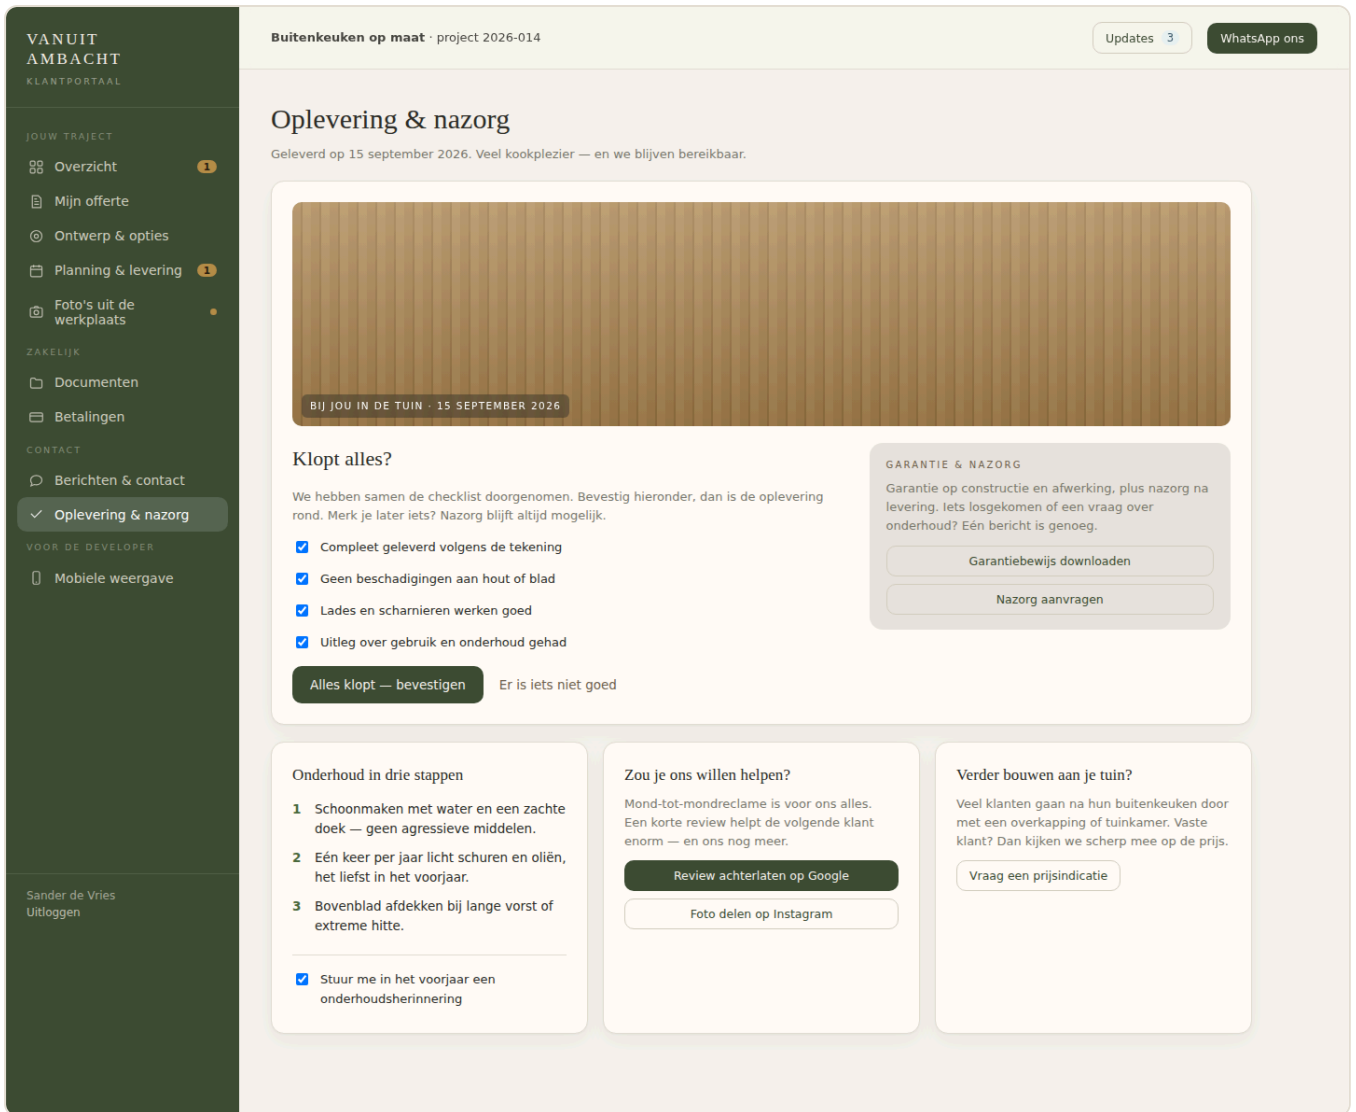

Screen 9 — Handover & aftercare (active after delivery).



Mobile designs: overview, quote reference and delivery proposal in phone view.

Mobile (emulated at 390 px wide)



Responsive behaviour at 390 px — Overview: sidebar becomes a bottom bar, actions on top.



Responsive behaviour at 390 px — Schedule & delivery.
